


**Urban Development and Housing Department
Government of Bihar**

Work Progress

May 2009

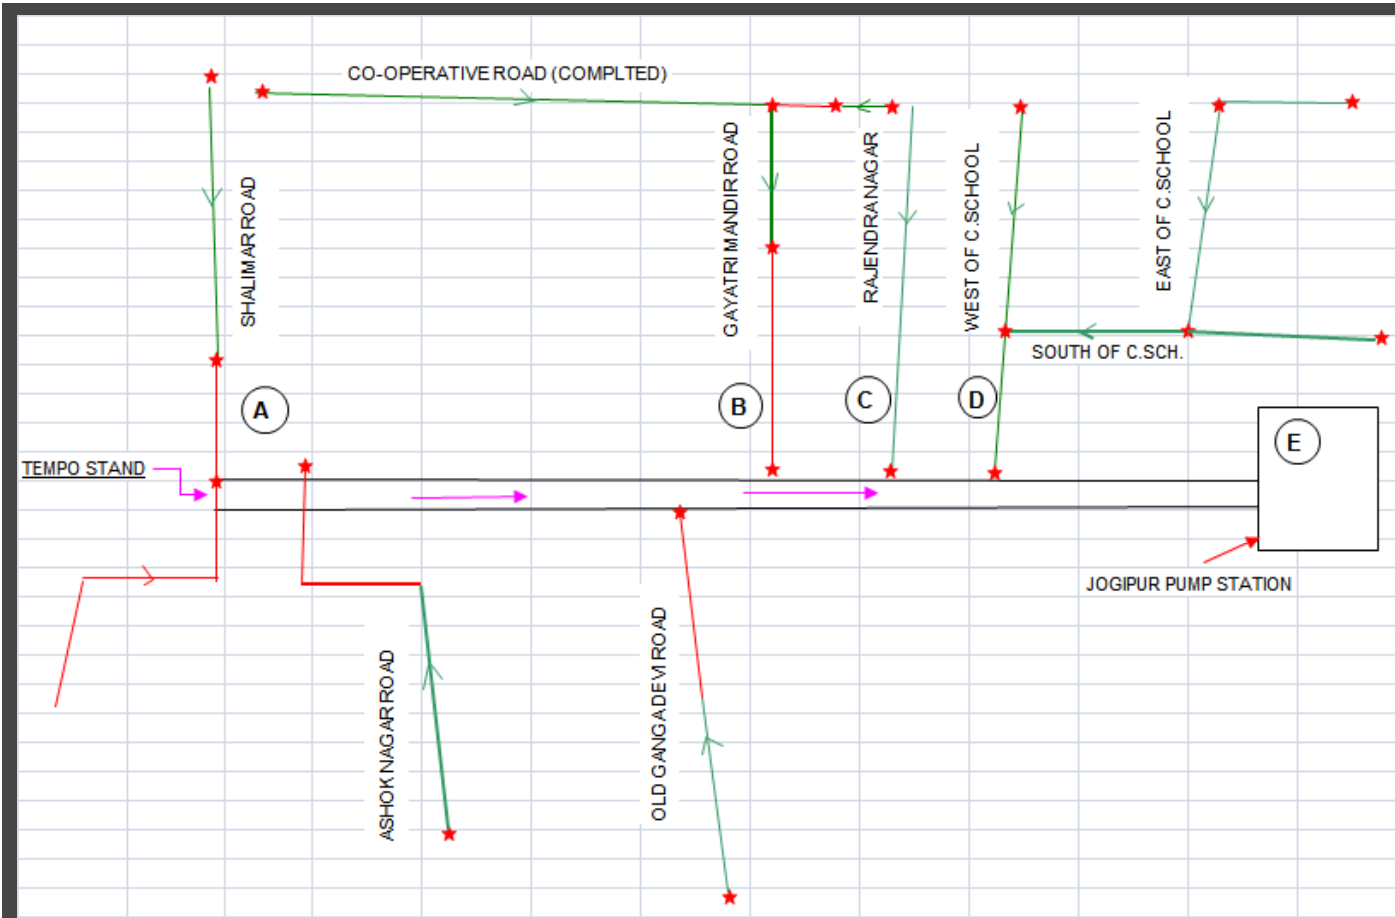


Completed lateral Drains



NBCC

KANKARBAGH DRAINAGE SYSTEM (TRUNK CHANNEL & LATERAL DRAINS)

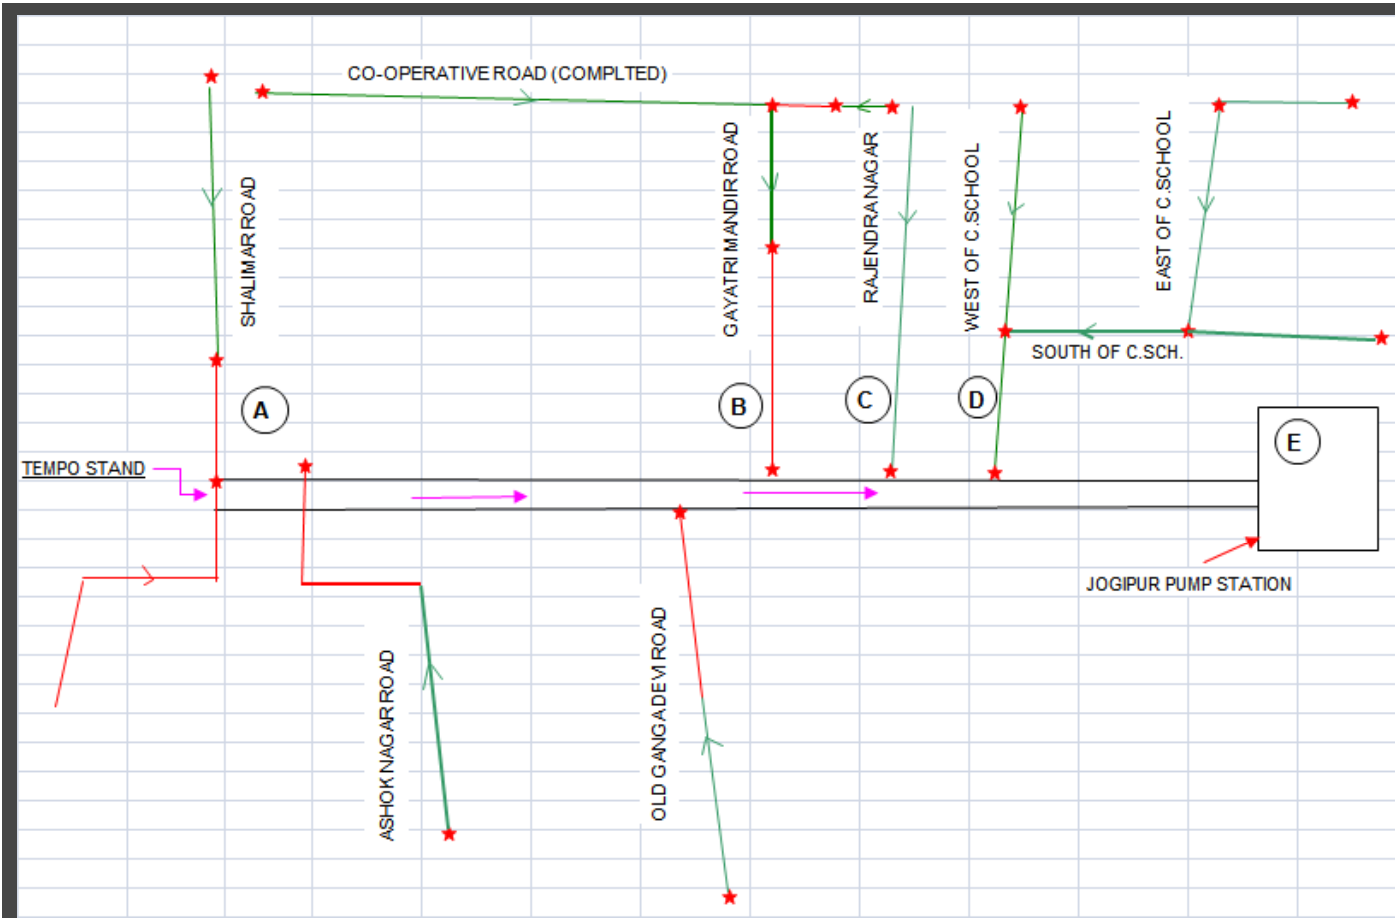

Completed lateral Drains



NBCC

KANKARBAGH DRAINAGE SYSTEM (TRUNK CHANNEL & LATERAL DRAINS)

Sl. No.	Locations	Total Length (in metre)	Completed Length.	Balance Length (in mtr.)	April-09	May-09	Date of Completion by NBCC	Department Perception
1	Lateral drain at West of Central School	500.00	460.00	40.00	0	15	31.05.09	On schedule
2	Lateral Drain at East of Central School	500.00	500.00	0.00			Completed	OK
3	Lateral Drain at South of Central School	385.00	360.00	25.00	0	15	31.05.09	On schedule
4	Lateral Drain at Gayatri Mandir Road	700.00	662.00	38.00	0	25	31.05.09	On schedule
5	Lateral Drain at Shalimar to Tampo Stand	1100.00	1020.00	80.00	0	55	05.06.09	On schedule
6	Lateral Drain at Co-Operative Road	860.00	860.00	0.00			Completed	OK
7	Lateral Drain at Rajendra Nagar Road	760.00	735.00	25.00	0	20	31.05.09	On schedule
8	Lateral Drain at Old Ganga Devi Road	490.00	490.00	0.00			Completed	OK
9	Lateral Drain at Ashok Nagar Road	400.00	355.00	45.00	0	25	31.05.09	On schedule

NBCC

Work Progress - Kankarbagh Drainage

10	Trunk Channel	1100.00	710.00	390.00		15.06.09	Doubtful
11	Outfall Channel Jogipur to Nandlal Chhapra	1843.00	1843.00	0.00		Completed	OK
12	Outfall Cahnnel Nandlal Chhapra to Pahari	2200.00	400.00	1800.00		25.06.09	On schedule
13	Pump House Jogipur					30.06.09	Doubtful
Grand Total—		10838.00	8395.00	2443.00	0 65 155		

Target- Achieve-

**** Hence Emergency measures after 31st May, 2009**

1. All missing links to be made ready temporarily.
2. Adhoc arrangements for pumping at new sump houses at Jogipur and Pahari are being provided by NBCC



Outfall - Before

Newly Constructed



NBCC

Work progress Kankarbagh Drainage

ACTIONS TAKEN AS PER RECOMMENDATIONS OF THE **TASK FORCE**

1	Total no. of Existing Pumps =105	Pumps made functional so far=88	Pumps to be functional by 31 st May,09=16
2	Total no. of Pumps to be replaced/added=60	Already Replaced=06	Pumps to be replaced/added by •07 th June,09=02 •31 st July,09=41
3	Emergency Stock of Pumps	<ul style="list-style-type: none"> • 27 Pumps@10HP : Already Available • 10 Pumps@22HP: By 31st May,09 • 10Pumps@32HP: By 31st May,09 	
4	Major Drains to be cleaned and Repaired=09	Already Repaired and Cleaned=05	By 31 st May,09, remaining 04
5	Medium and small drains=651	Already Cleaned=497	By 31 st May, 09=154
6	<u>Monitoring and Supervision arrangements (S.O.P)</u> <u>Comprehensive Action Plan</u>	<ul style="list-style-type: none"> • Central Control Room • 13 Static Team • 06 Mobile Team 	To be started from 1st June,09

Patna Municipal Corporation

(All the Cost Parameters are Rs. in Crore)

Sl. No.	Name of Sector	Allocation of Central Share (2005-2012)	<u>Admissible Project Cost as per Central and State Allocation</u>	Total Sanctioned Project Cost	Balance	<u>Project Submitted to Govt. of India</u>
1	JNNURM - UIG	442.41	884.82	758.36	126.46	293.92
2	JNNURM - BSUP	496.54	993.08	709.98	283.10	Nil
3	JNNURM - UIDSSMT	254.78	318.48	1207.54	-889.06	691.70
4	JNNURM - IHSDP	140.06	175.08	194.11	-19.03	190.24
	TOTAL	1333.79	2371.46	2870.00	-498.54	1175.86

JNNURM Schemes

New Initiatives –

Target is to take up all important roads of Municipal Corporations.

Sl.No	ULBs	No. of Roads - Sanctioned	Allocated Amount (in Rs. Lakh)
1	Patna Municipal Corporation	94	5003.00
2	Gaya Municipal Corporation	117	800.00
3	Bhagalpur Municipal Corporation	39	717.00
4	Muzaffarpur Municipal Corporation	57	760.00
5	Darbhanga Municipal Corporation	40	965.36
6	Biharsharif Municipal Corporation	12	736.2727
7	Arah Municipal Corporation	102	870.11
	Sub Total (Municipal Corporations)	461	9852.4427
	Nagar Parishad – 26	61	2417.5366
	Nagar Panchayat – 29	7	730.0181
	Total	529	12999.9975

New Initiatives

1. Development of Roads

New Initiatives – To take Major Parks.

1. Buddha Smirti Park:

- Estimated Project Cost - 150.53 Crores.
- Target Date of Competition – November 2008
- Expected Date of Completion – December 2009.

2. **Shahid Veer Kunwar Singh Azadi Park (Area – 20.71 Acres)**

- To be developed under Public Private Participation (PPP) Model.
- Proposals were called four times due to inadequate participation of Contractors.
- Consortium of M/s Vijeta Projects – Kaushal Kanchan were awarded the work for the same.
- Estimated Project Cost – 35.37 Crore
- Payment Terms:
 - Upon signing of Concession Agreement - Rs. 1 Crore
 - Every 6 month as Concession Payment up to 30 yrs - Rs. 26 Lakh
 - (at the increment rate of 5 % every year)

New Initiatives

2. Development of Parks

New Initiatives – To take Other Small Parks.

<u>Other Small Parks</u>			
Sl.No	ULBs	Approved No. of Parks	Approved Amount (in Rs. Lakh)
1	Patna Nagar Nigam	30	1680.40
2	Bhagalpur Nagar Nigam	02	60.00
3	Gaya Nagar Nigam	24	218.50
4	Darbhangra Nagar Nigam	02	90.00
Sub Total		58	2048.90
Nagar Parishad – 09		33	480.11
Nagar Panchayat - 04		04	71.82
Total		95	2600.60

New Initiatives

3. Development of other Small Parks

The Department has taken decisions to improve all major Ghats before next CHHAT Festival.

GHATS / TALABS

Sl.No	ULBs	Approved No. of Ghats / Talabs	Approved Amount (in Rs. Lakh)
1	Patna Nagar Nigam	21	1150.00
2	Darbhanga Nagar Nigam	18	221.05
3	Arah Nagar Nigam	10	500.00
4	Bhagalpur Nagar Nigam	16	207.00
5	Muzaffarpur Nagar Nigam	05	240.00
6	Gaya Nagar Nigam	14	170.95
Sub Total		84	2489.00
Nagar Parishad – 16		97	1219.19
Nagar Panchayat – 16		31	346.06
Total		212	4054.25

New Initiatives

4. Development of Ghats

New Initiatives :

Ganga River Front Development

1. Development of all important Ghats.
2. Starting ferry services between Collectrate Ghat to Bhadragehat.
3. To link Harminder Saheb and Patan Devi Mandir with the Ganga Ghats by foot over Bridge.

New Initiatives :

Solid Waste Management

1. Schemes for Solid Waste Management has been approved for the Towns Patna and Patna Urban Agglomeration Area (PUA), i.e. Khagaul, Danapur and Phulwarisharif.
2. Door to door collection of Solid Waste and its disposal at Disposal Site to start from 15th October, 2009

New Initiatives :

Citizens Computerized Grievance Redressal Cell (CCGR)

1. **Citizens Computerized Grievance Redressal Cell (CCGR)** has been established to monitor all existing control rooms established in 7 Municipal Corporations of Bihar.
2. One single toll free telephone number 15331 to be in place from 30th June 2009 from any part of Bihar can complain about Municipal Services.
3. This cell will also facilitate provision of the following services to the public a) Carpenter, b) Plumber, c) Fridge, d) AC, e) Electrician, f) Taxi services also.

ISSUES

1

- **New Township Development.**

2

- **Officers Shortage.**

3

- **City Bus Services : Selection of Agency**

4

- **Slum Area Development : Land Acquisition**



THANK YOU
